

SMARTBRIDGE PROJECT SUBMISSION

PHASE 4 – Project Planning

Auto Ticket Classification using Flow Designer

Project Details

Date: 29/09/2026

Team ID: 6ab4dd8ca238dc999eb5dd5c-Team ID

PROJECT PLANNING PHASE

Phase 4 – Project Planning

Project Title	Auto Ticket Classification using Flow Designer
Phase	4 – Project Planning Phase
Project Domain	IT Service Management / Workflow Automation
Planning Objective	Define tasks, schedule, resources, milestones, risks and deliverables for project implementation

1. Project Planning Overview

The Project Planning Phase defines how the Auto Ticket Classification using Flow Designer project will be implemented, monitored and completed. The plan divides the project into manageable activities covering environment setup, workflow development, classification rules, testing, documentation and demonstration.

2. Project Objectives

- Set up the required platform and project environment.
- Configure the ticket fields and classification structure.
- Develop the automated classification and routing workflow using Flow Designer.
- Create and validate classification rules for common support issues.
- Test the workflow with different ticket scenarios.
- Document the implementation and prepare the final demonstration.

3. Work Breakdown Structure (WBS)

WBS ID	Activity	Main Deliverable
1.0	Project Setup	Platform/environment ready
2.0	Ticket Configuration	Ticket fields and categories configured
3.0	Classification Design	Classification rules prepared
4.0	Flow Development	Flow Designer workflow implemented
5.0	Assignment & Notification	Routing and notification actions configured
6.0	Testing	Test cases and results
7.0	Documentation	Project report and technical documentation
8.0	Demonstration	Working project demonstration

4. Project Schedule

Week	Planned Activity	Expected Output
Week 1	Project setup and requirement review	Environment and requirements confirmed
Week 2	Ticket fields, categories and data configuration	Ticket structure ready
Week 3	Classification rules and workflow design	Rules and flow logic finalized
Week 4	Flow Designer development	Initial working automation
Week 5	Assignment, priority and notification configuration	Complete workflow
Week 6	Functional testing and bug fixing	Validated workflow
Week 7	Documentation and GitHub phase update	Project documentation
Week 8	Final demonstration and submission	Final project package

5. Resource Planning

Resource Type	Required Resource	Purpose
Platform	ServiceNow / Flow Designer environment	Develop and execute the automated workflow
Software	Web browser and development tools	Configuration and documentation
Repository	GitHub public repository	Maintain project files phase-wise
Documentation	Word/PDF/PPT tools	Prepare project report and presentation
Testing Data	Sample support tickets	Validate classification and routing
Team	Student project team / individual developer	Planning, development, testing and documentation

6. Task Responsibility Plan

Task	Responsible Role	Completion Criteria
Requirement review	Project Student / Team	Requirements documented
Platform configuration	Developer	Required environment available
Ticket configuration	Developer	Fields/categories configured
Flow development	Developer	Flow executes successfully
Testing	Developer / Tester	Test cases executed and defects recorded
Documentation	Documentation Lead / Student	Report and GitHub files updated
Demonstration	Project Student / Team	Working workflow demonstrated

7. Milestones

Milestone	Expected Result
M1 – Planning Complete	Project scope, activities and schedule finalized
M2 – Configuration Complete	Ticket structure and categories ready
M3 – Prototype Complete	Initial classification flow working
M4 – Automation Complete	Classification, assignment and notification integrated
M5 – Testing Complete	Workflow validated using test scenarios
M6 – Submission Ready	Documentation, GitHub repository and demonstration prepared

8. Risk Management Plan

Risk	Impact	Mitigation
Incorrect classification rule	Ticket may be routed incorrectly	Test multiple examples and refine conditions

Risk	Impact	Mitigation
Flow execution error	Automation may stop or fail	Validate each flow action and use error handling
Incomplete ticket data	Classification may be uncertain	Use default/fallback category and manual review
Configuration changes	Existing workflow may be affected	Document changes and test after modifications
Insufficient testing	Defects may remain before demonstration	Use positive, negative and edge-case test scenarios

9. GitHub Phase-wise Submission Plan

Folder / Phase	Planned Contents
01_Brainstorming_Ideation	Problem statement, ideas and selected project concept
02_Requirement_Analysis	Functional and non-functional requirements
03_Project_Design	Architecture, workflow and design document
04_Project_Planning	This planning document, schedule, WBS and risk plan
05_Project_Development	Flow configuration details, screenshots and implementation files
06_Project_Testing	Test cases, expected/actual results and defect records
07_Project_Documentation	Final report, user guide and supporting documents
08_Project_Demonstration	PPT, demo screenshots/video reference and final presentation material

10. Expected Planning Outcome


At the end of the planning phase, the project team will have a clear implementation schedule, defined responsibilities, required resources, milestones, risk controls and GitHub submission structure. This plan provides the baseline for moving into Phase 5 – Project Development.

Prepared for: SmartBridge Project Submission


Project: Auto Ticket Classification using Flow Designer | Phase 4 – Project Planning

Project Details & Implementation Evidence

Date: 29/09/2026 Team ID: 6ab4dd8ca238dc999eb5dd5c-Team ID

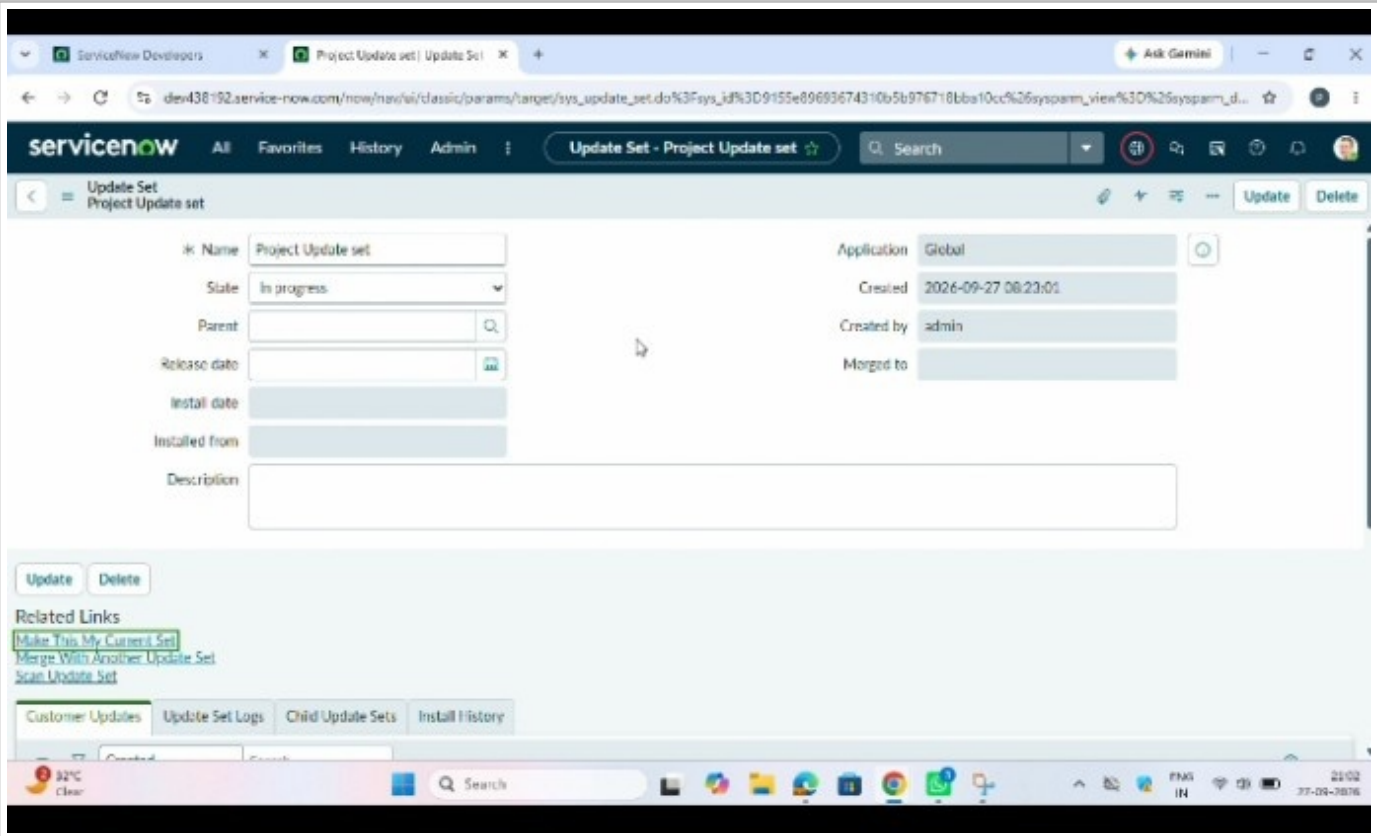


Implementation Screenshot 1

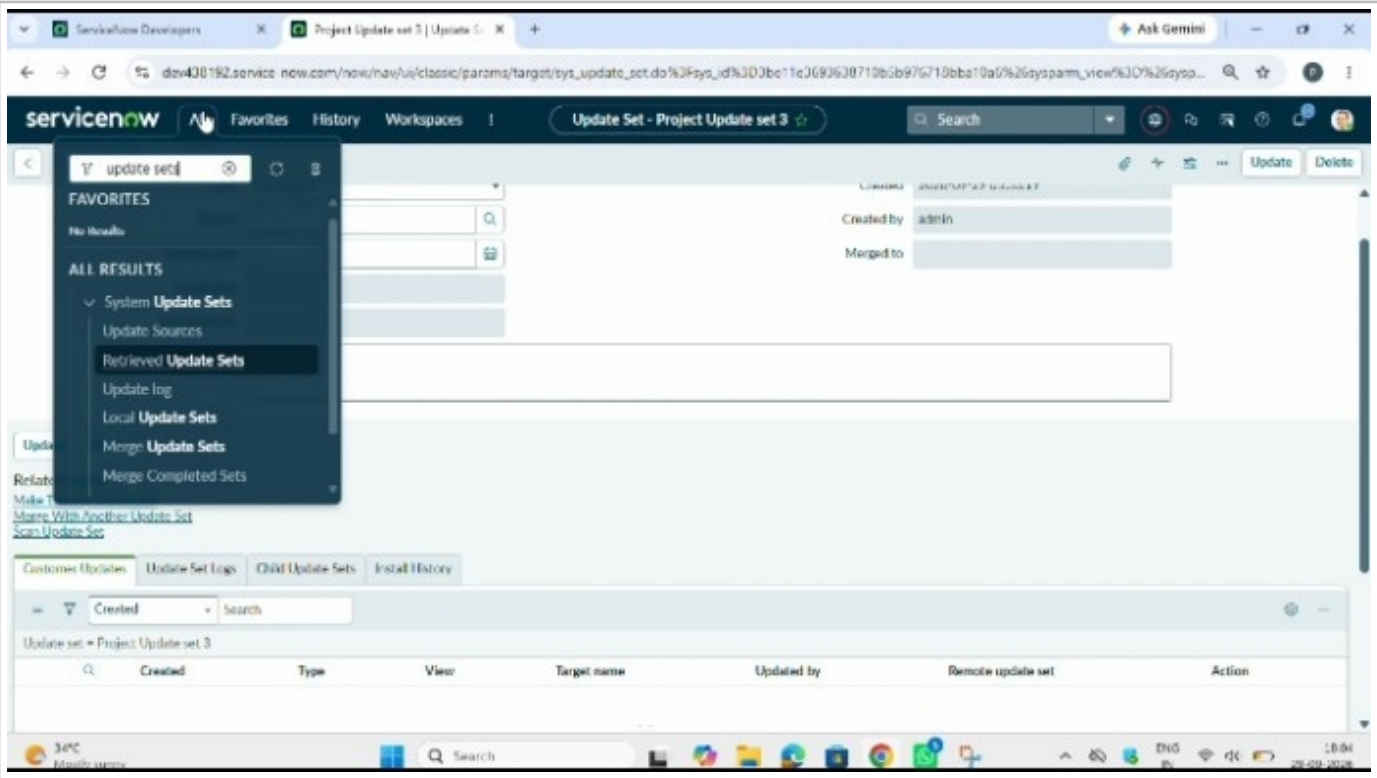

Implementation Screenshot 2

Implementation Evidence – Screenshot 3

Date: 29/09/2026 Team ID: 6ab4dd8ca238dc999eb5dd5c-Team ID

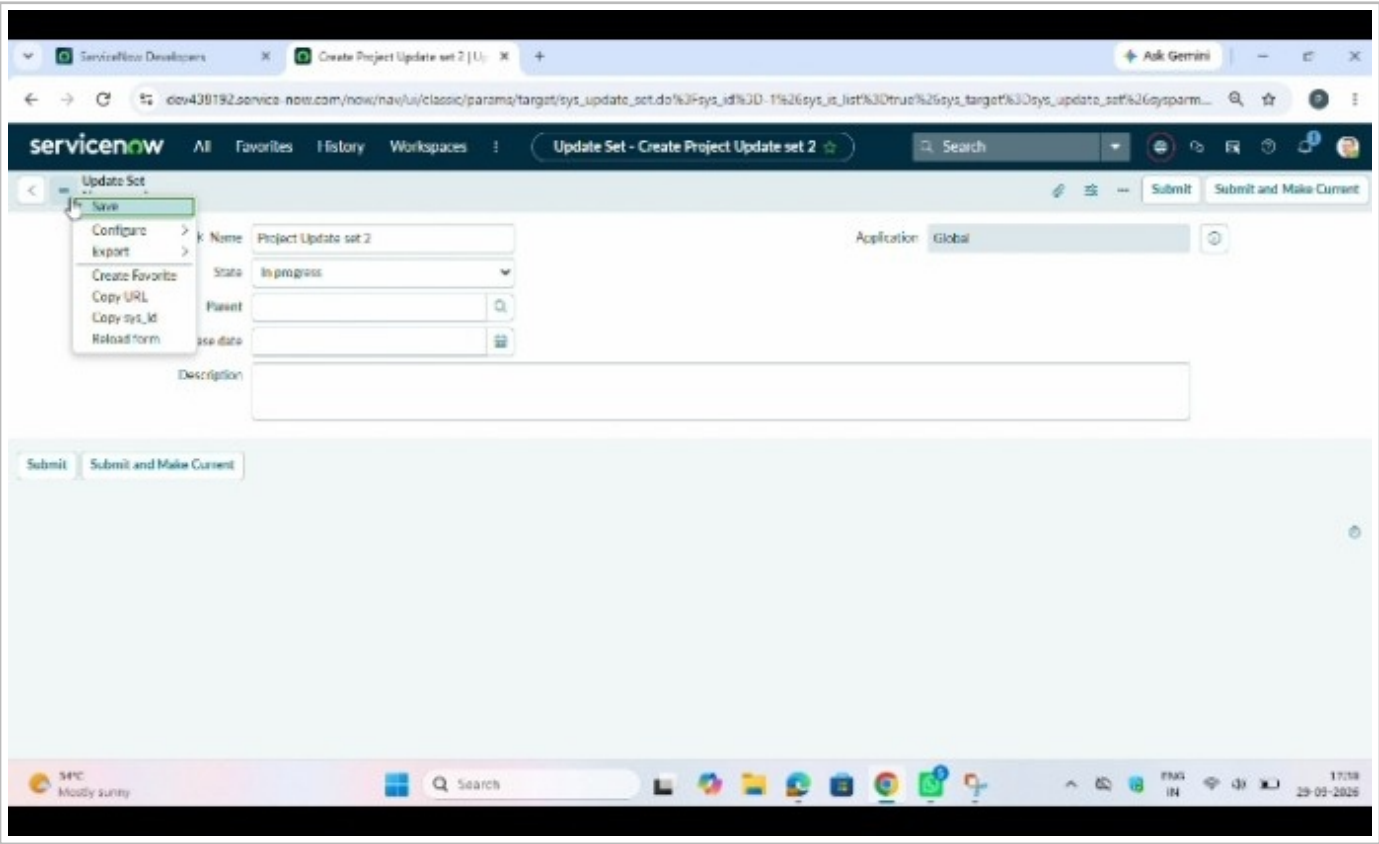

Implementation Screenshot 3
